



CASCADE RADON, INC.
Testing, Mitigation,
Systems Design
CCB 180537 / CASCARI927C1

12839 NE Airport Way Bldg. 9
Portland, OR 97230
Phone: (503) 421-4813
Fax: (503) 281-6170
Office@CascadeRadon.com

Radon Survey Analysis Job # 18-C108R

for

Silver Falls School District
Evergreen School
c/o Lorin Stanley

property located at

3727 Cascade Hwy.

NE Silverton, OR, 97381

February 13, 2019



STATE OF OREGON
CERTIFIED
EMERGING SMALL BUSINESS

Introduction

The following report documents a study of radon levels for the property located at 3727 Cascade Hwy. NE Silverton, OR, 97381. The goal of this study is to determine indoor radon levels within the areas addressed by the mitigation system following system installation.

Analysis assumes that the building tested was maintained under “closed-building” conditions (windows closed and exterior doors shut immediately after entering and exiting) 12 hours prior to the start of testing, as well as normal indoor temperatures, for the duration of the testing period.

Conclusions and Recommendations

The radon mitigation system has been installed per applicable codes. The average “Short-Term” test levels are now below the EPA recommended “action level” of 4.0 pCi/L. Test performed was a “Short-Term” post-mitigation diagnostic test, with a duration of 72 hours.

No mitigation action is recommended at this time. The EPA recommends that in buildings with mitigation systems, mitigated areas undergo post-mitigation testing using a long-term, Alpha-Track type test for a duration of 12-months. Alpha-Track test kits are available for about \$25-30 each.

All conditions, warranties, and guarantees noted in the Contract are transferable to future owners of the same property. For further information regarding the system and long-term testing, post-mitigation radon testing, please refer to the Mitigation Contract or the document titled “About Your Radon System” provided to you.

Note: The EPA recommends that testing be conducted in areas that were mitigated at least every 2 years to ensure that the system remain effective.

Short-Term, Post-Mitigation Test Results:

Manometer Reading: 2.2 inches of water column pressure.

The building tested was assumed occupied during testing.

The measurement technique used (1) Rad Star continuous electronic monitors: (2045).

Measurements of radon levels were made in the following areas:

Test End: 11:45 AM, 1/18/2019

Monitor ID 2045–Grade 6th, 7th, and 8th classroom

Average radon reading for duration of test = 0.7 pCi/L

Highest level recorded: 2.0 pCi/L

Lowest level recorded: 0.0 pCi/L

Key:

pCi/L: Picocuries per liter – units of radon concentration.

Average: Cumulative average of the entire period since the test started.




Please contact me if you have any questions.

Thank you,

Danielle Weir
NRPP 108953 RT

Test Location Map

EVERGREEN SCHOOL

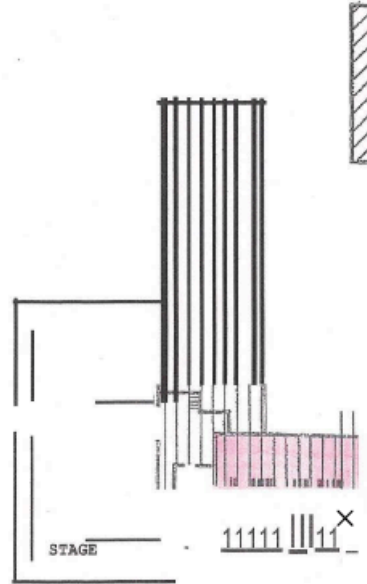

1Rm
Grade 6/7/8
with 1CRm




FIRST FLOOR

- CJ ORIGINAL BUILDING
- EZ2] 1874 AOOrrION
- [ill UNIQOWEH



Test Results Map

EVERGREEN S CHOO

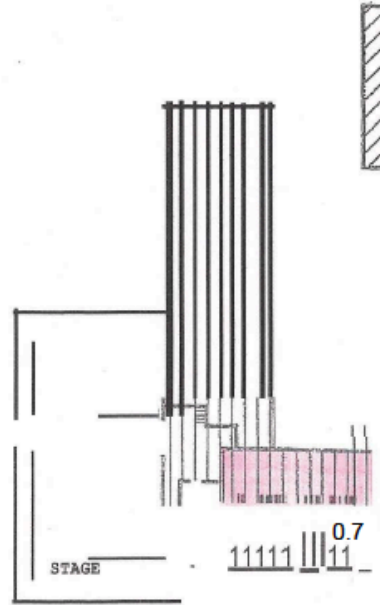

1Rm
Grade 6/7/8
with 1CRm

- CJ ORIGINAL BUILDING
- EZ2] 1874 ADDITION
- [ill UNKNOWEH

